


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0714
TRUNK HIGHWAY 22
COUNTY Blue Earth
DISTRICT 7A

LIMITS: East Jct. T.H. 14 Jct. T.H. 60 in Mankato - N. Co. Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
1928	169-5-32-1A	Grading Br. N#4768 Br. N#4769	40' 27' 27'		530 D.T. & B.S.-O.H. 378 D.P.G.-O.H.
1928	169-5-32-1A	Concrete	20'	7 1/2"	Widened by City.
1929	169-5-32-1A	Gravel	24'	2"	1000 C.Y./Mile.
1930	169-5-32-1A	Concrete	20'	9-7-9	
C	1949 A.F.E. 37	Gravel Base (1) Bit. Surfacing Mixed Bit.	36' 24'	2-12" 1 1/2"	R.T.B. 3465 Gal. Agg. 375 C.Y. (Mixed Prime)
C	1950 A.F.E. 4	Bit. Surfacing Plant Mix Bit.	24'	1 1/2"	MC-3, 140 Gal. AC-1, Bit. Mixture, 286 Tons
C	1954 (2) 0714-02	Widening Cr. Rock Base (0.61 MI) Plant Mix Bit.	36' 36'	12" 3 1/2"	40-20' rdwy. widened to 56'
C	1954 (2) 0714-04	Bit. Stab. Base * Plant Mix Bit. Truck Lane (1.07 MI)	Var. 24'	3"	* On old conc. which was widened with Gray. or Bit. Base
M	1964 SF	Spot Bit. Repair	24'		PL Mix 118 Tons MC-3, Tack 40 Gal.
M	1965 C	Light Bit. Seal	24'		RS-1C, 7534 Gal. Agg. 303 C.Y.
C	1969 0714-07	Rt. Turn Lane			Jct. C.S.A.H. 2
C	1971 0714-12	Grading, Bit. Base Asphaltic Conc.	24'	1 1/2"-2"	

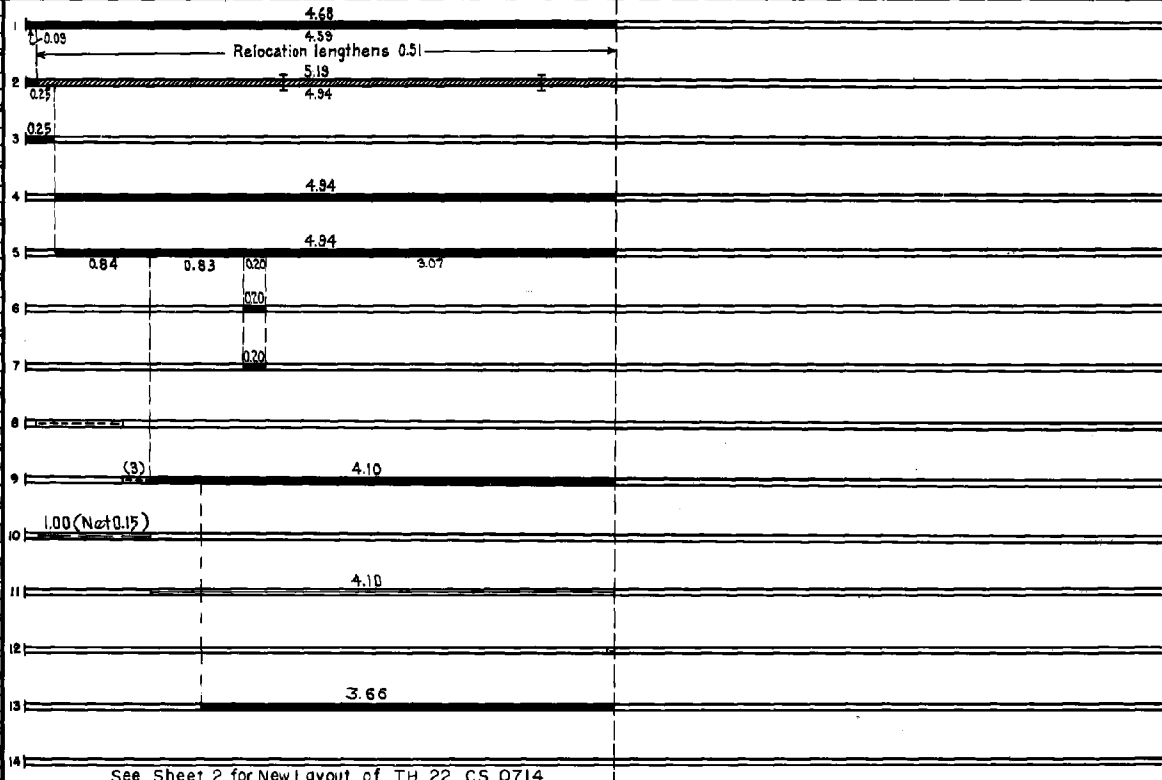

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1927	4.68	3.26	0.00	1.42	0.00	3.26	0.00	1.42	0.00
1928		5.19	4.18	0.17	0.84	0.00	4.18	0.17	0.84	0.00

REMARKS: Layout is to scale as of 1928
(1) Old concrete buried (2) Contract not final but work substantially complete (3) Concr. imp. widened 2' Rt. & Lt. with Plant Mix Bit. on Bit. Stab. Base.

