


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1508
TRUNK HIGHWAY 223
COUNTY Clearwater
DISTRICT 2A

LIMITS: Jct.T.H.92- Jct.C.R.III in Leonard
Ref. Pt. 000+00.000 - 007+00.644



YEAR BUILT	PROJECT No	DESCRIPTION			CODE No Dist.
		TYPE	WIDTH	THICKNESS	
		Gravel	24'		
M 1970	A.F.E. 26	Spot Sand-Grav Base Spot Grav. Resurface	24'		
C 1959	1508-02	Grading Gravel	Var.	10,682 Tons	1458
C 1960	1508-03	Gravel Base Plant Mix Bit Curb & Gutter in Leonard	24' 1 1/2"	502 Tons Bit. Mat'l.	160
M 1966	C	Light Bit. Seal	24'	RC-250, 14759 Gal. Agg. 487 C.Y.	1066
C 1972	1508-05	Plant Mix Bit. O.L.	24' 1 1/2"		372
M 1984	1508 F r A1	Bituminous Seal Coat		CRS-1 21,523 Gal. Agg. 769 C.Y.	
M 1992	M4555	Bit. Overlay	Var. 1 1/2"	Spec. 2341	
M 1999	8822-06	Agg. Seal		Fine, Agg. Number 2	
S 2008	1508-07	Milling Bit. Overlay	28' 1 1/2"	Spec. 2360	
	2012	8822-136	Bit. Seal Coat	28'	

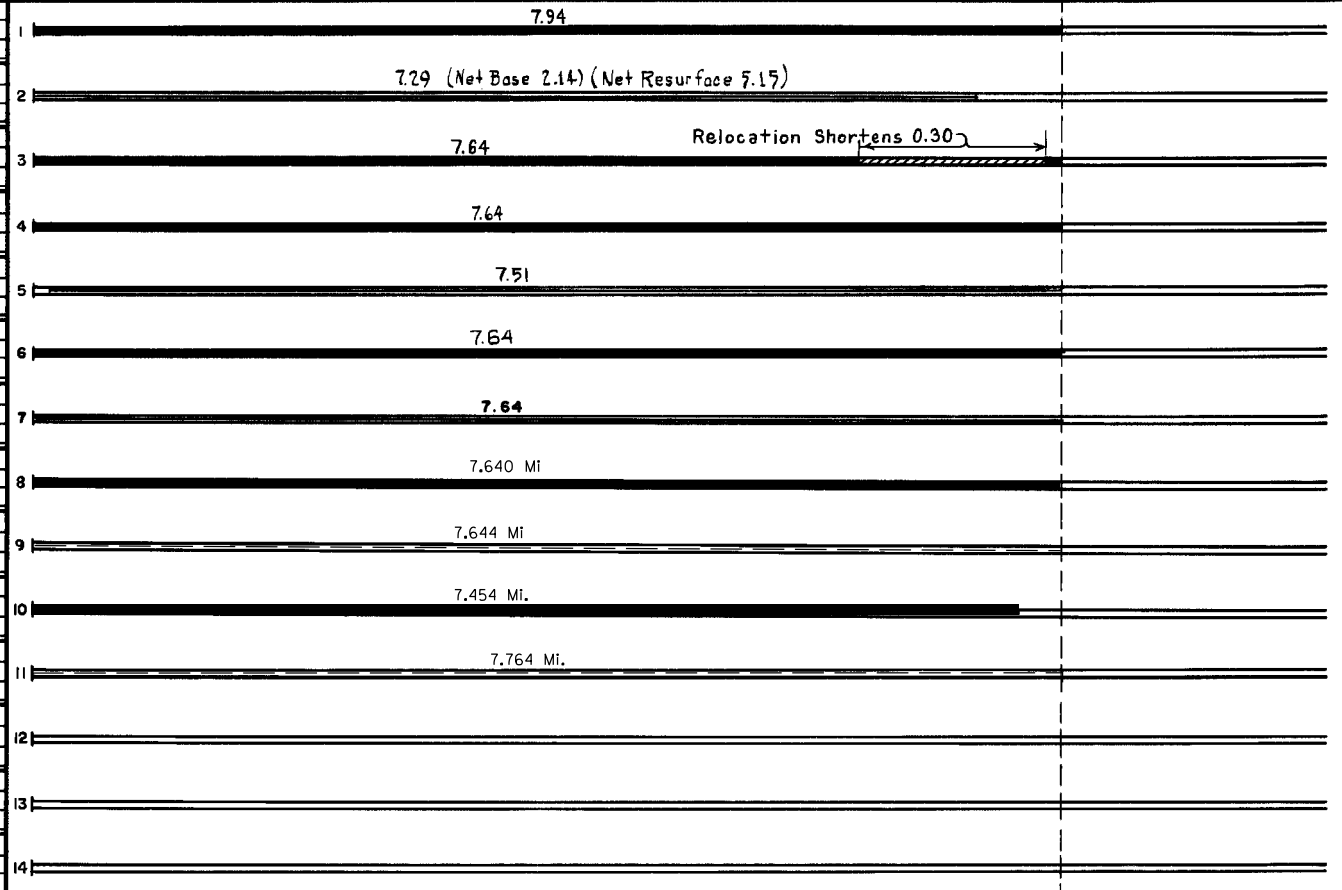

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1958	7.94	7.40	0.00	0.54	0.00	7.94	0.00	0.00	0.00
1959		7.64	7.03	0.00	0.61	0.00	7.64	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949
