

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3418
TRUNK HIGHWAY 4
COUNTY Kandiyohi
DISTRICT 3B

LIMITS: Jct. T.H. 55 - N. Co. Line

Ref. Pt. 143+00.193 - 145+00.048


PLAN



Kandiyohi Co.
Stearns Co.

SCALE: 1/4 MI.

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1941	3418-01	Grading Stab. Gravel	36'		
					0.33 Mi. Divided Highway Grav. 1363 C.Y./Mi.
1942	A.F.E. 7	Seeding			
					Seed supplied by R.S.D. (S.P. 3418-03) Maint. Dept.
1947	3418-04	Stab. Gravel	28' 6"	9"	
1948	3418-05	Mixed Bit.	26' 5"	1"	
1952	A.F.E. 5	Light Bit. Seal Coat	24' 30"		
					RC-2, 3015 Gal. Agg. 145 C.Y.
1955	3418-06	Plant Mix Bit.	24' 30"	1 1/2" added	
1956	A.F.E. 605	Bit. Seal Coat	24' 48"		
					RS-2, 7220 Gal. Agg. 270 C.Y.
1958	A.F.E. 605	Bit. Seal Coat	25'		
					RC-2, 4462 Gal. Agg. 122 C.Y.
1979	2412-02	Bit. Surfacing Bit. Shoulders	24' 9 1/2"	3'	
					Sp. 2241 Right Turn Lanes
1996	3418-09	Bit. Overlay Bit. Shoulder	24' 1 1/2"	3'	
					Spec. 2341 Spec. 2341
1999	M99050	Crack Repair			
2002	8823-36	Bit. Seal Coat			
					Type FA2
2007	8823-99	Agg. Seal			
					FA-3

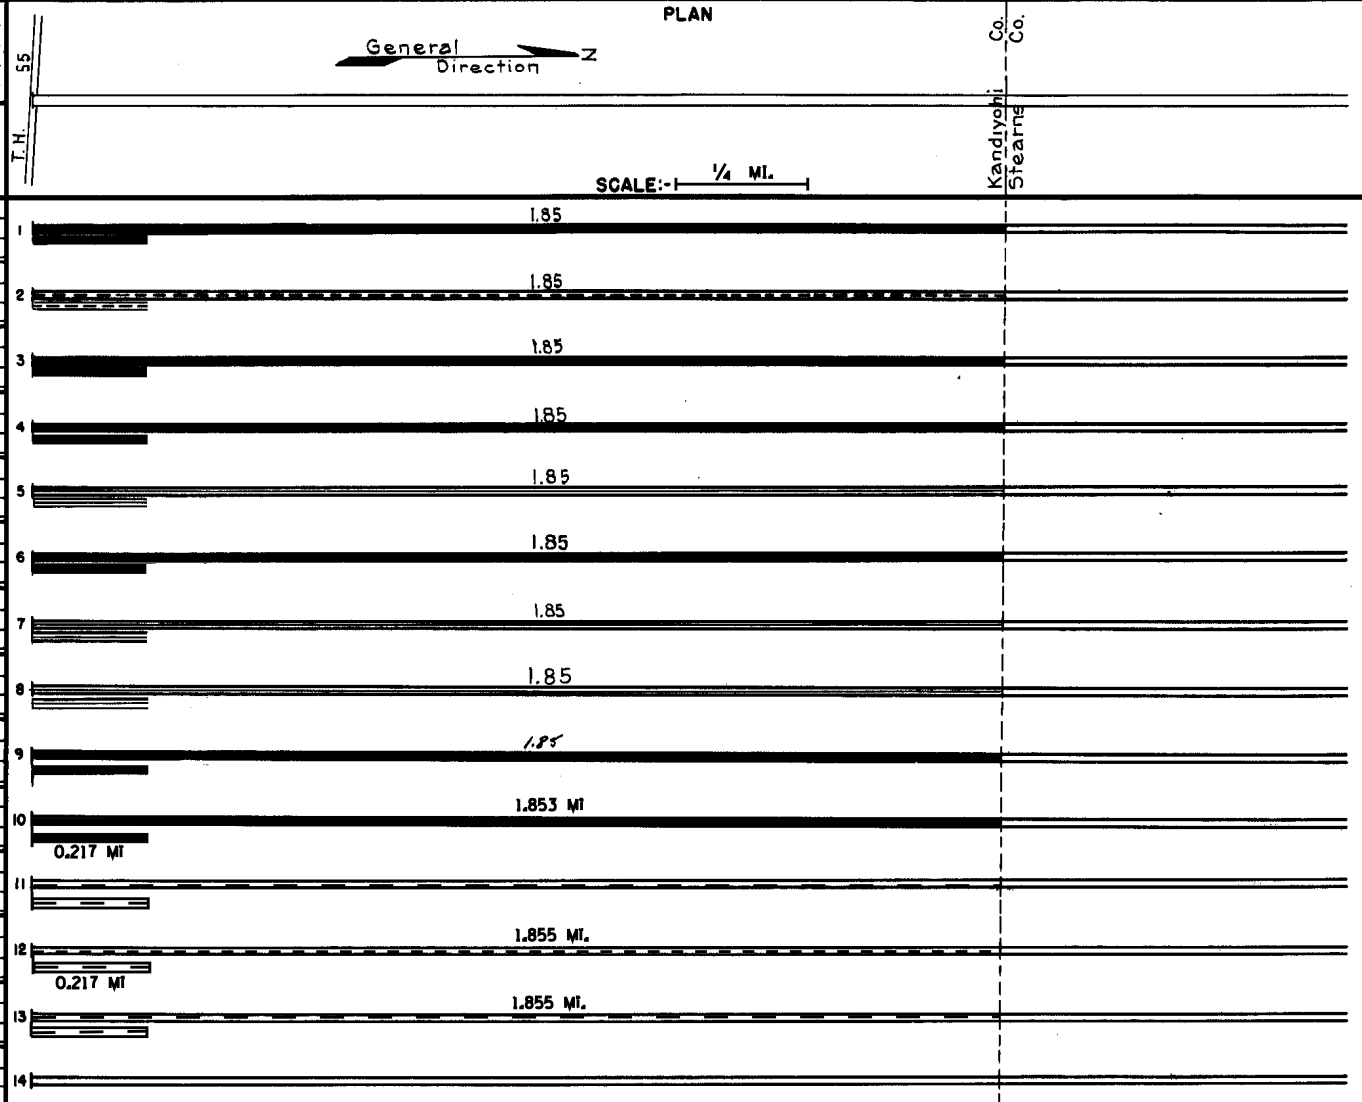

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1941		1.85	1.85	0.00	0.00	0.00	1.85	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1941
