


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5907  
TRUNK HIGHWAY 268  
COUNTY Pipestone  
DISTRICT 88

LIMITS: Jct. T.H. 75 - Jct. C.S.A.H. 18



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1942	59-502-01	Grading	26'		Added in 1949
1942		Gravel	26'		Built by County 800 CY/Mi. Added in 1949
		Br. 6407 & Br. 6406	27'		No Record of Const 48' x 120' Timber Added in 1949
M	1949 A.F.E. 6	Grav. Resurfacing	24'		4702 Tons
C	1970 A.F.E. 30	Sand-Gravel Base	30'	3'-6"	SC-2 & 3, 81842 Gal. Agg. 4988 Tons
		Bit. Surfacing	24'	1"	
		Mixed Bit.	24'	1"	
M	1952 A.F.E. 4	Spot Treat.	24'		RS-2 & MC-2, 15240 Gal. Agg. 730 C.Y.
		Bit. Surf. Repair	24'		
		Light Bit. Seal (6.76 Mi)	24'		
M	1954 A.F.E. 604	Spot Treat.	24'		SC-3 & MC-2, 9326 Gal. Agg. 633 Tons
		Bit. Surf. Repair	24'		
M	1955 A.F.E. 604	Spot Treat.	24'		SC-3, 9558 Gal. Agg. 717 Tons
		Bit. Surf. Repair	24'		
M	1956 A.F.E. 604	Spot Treat.	24'		SC-3 & MC-2, 14404 Gal. Agg. 1126 Tons
		Bit. Surf. Repair	24'		
C	1955 59-501-07	Gravel Base	26 1/2"	6"	Transferred into T.H. System in 1958
		Mixed Bit	22'	1"	
		Br. 6405	28'		72' T. T. S.
C	1958 5907-02	Plant Mix. Bit.	24'	2"	
		Stab. Grav. Shoulders	24'	added	
M	1959 A.F.E. 605	Light Bit. Seal	25'		RC-2 & RS-2, 17069 Gal. Agg. 602 C.Y.
M	1966 C	Light Bit. Seal	25'		CRS-1, 17031 Gal. Agg. 576 C.Y.
C	1971 SF	Pl. Mix. Bit. Surf.	24'	1 1/2"	

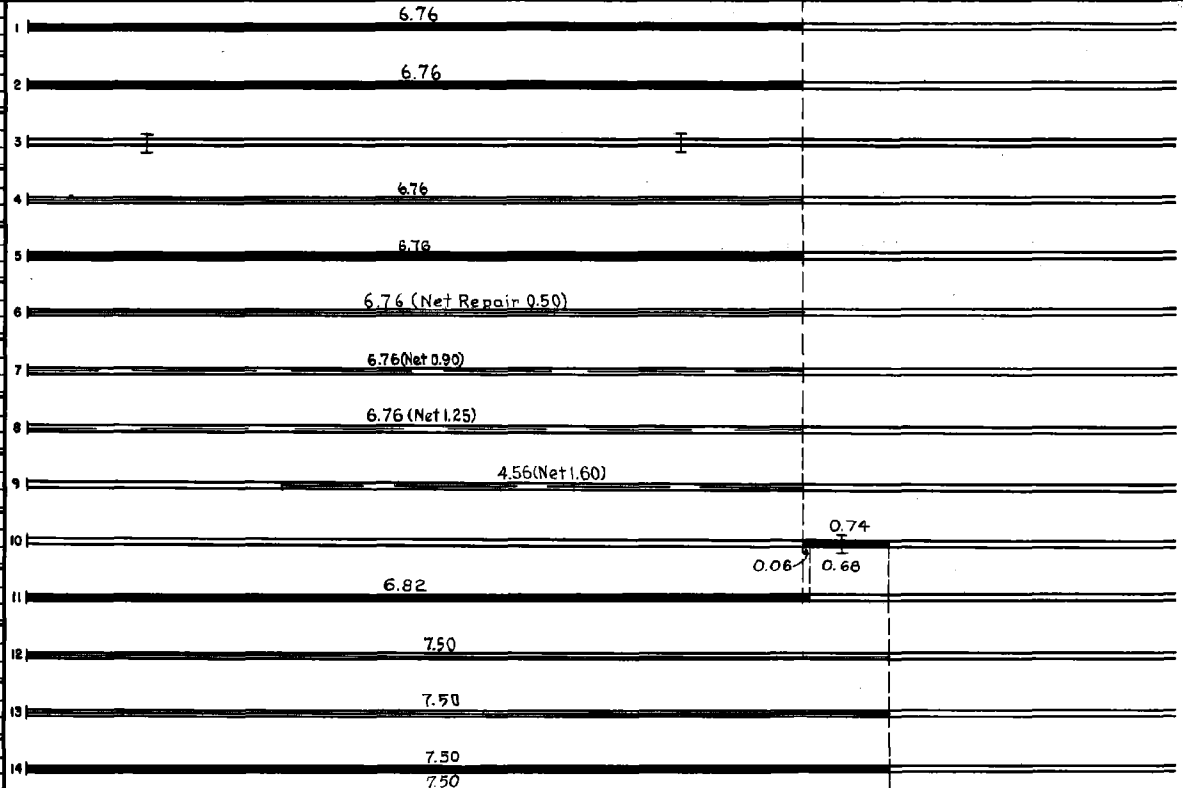

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1957	6.76	4.74	0.02	1.99	0.01	6.73	0.03	0.00	0.00
1958	1960	7.50	5.98	0.02	1.48	0.02	7.46	0.04	0.00	0.00
1960		7.50	5.98	0.02	1.48	0.02	6.48	0.02	0.98	0.02

REMARKS: Layout is to scale as of 1949

