


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6615
TRUNK HIGHWAY 298
COUNTY Rice
DISTRICT 60

LIMITS: In Faribault
Jct. T.H. 60 - Mn. Correctional Facility
Ref. Pt. 000+00.000 - 001+00.151



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Bit. Concrete	36'		No Record of Const. Added in 1951
		Mixed Bit.	15-30'		No Record of Const. Added in 1951
		Combination Type	35'		
		Mixed Bit	17'		No Record of Const. Added in 1951
		Gravel	18'		
M 1952	A.F.E. 4	Bit. Surf. Repair	24'		SC-2, 5818 Gal. Agg. 306 C.Y.
M 1953	A.F.E. 604	Spot Treat.			Bit. 6500 Gal. Agg. 297 C.Y. (Net Repair 0.50 Mi.)
	A.F.E. 711	Bit. Surf. Repair	22'		
		Straighten Sidewalk			
M 1954	A.F.E. 604	Spot Treat.			MG-2, 2425 Gal. Agg. 172 Tons (Net Repair 0.25 Mi.)
		Bit. Surf. Repair	24'		
M 1956	A.F.E. 605	Light Bit. Seal	20 3/4'		RS-2, 1500 Gal. Agg. 40 C.Y.
C 1961	6615-02	Grading			
		Gravel Base	2 1/2" 6"		on 9" Gravel Sub-Base
		Plant Mix Bit.	2 1/2" 3"		
M 1966	C	Bit. Seal Coat	25'		CRS-2 Bit. 3655 Gal. FA-2 Agg. 115 C.Y.
M 1995	M95195	Bit. Mill. & Overlay	26' 1 1/2"		Spec. 2341
2013	Turnback Shorten	Part of L.R. 298 CS 6615			Effective Oct. 15, 2013

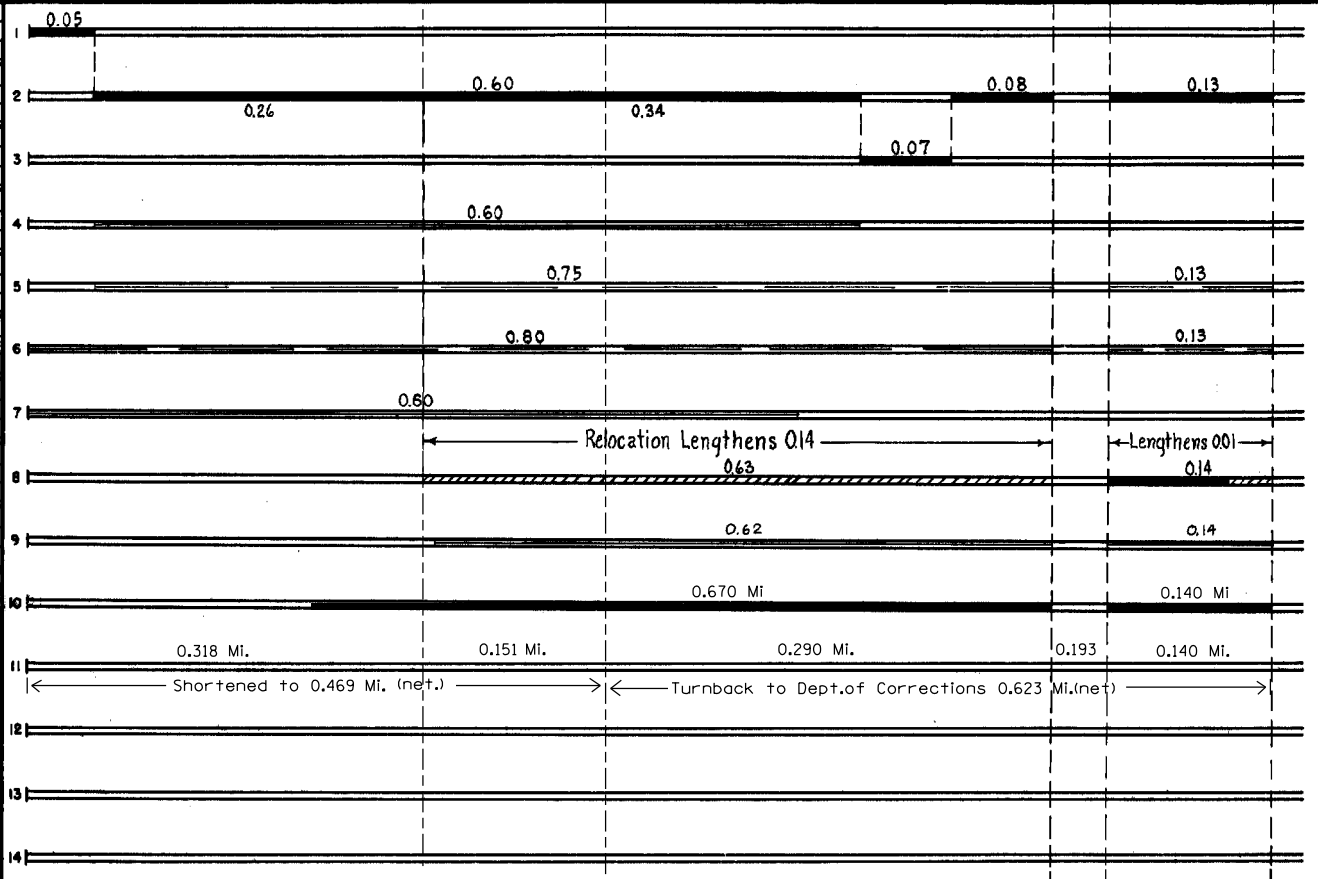

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1951	1960	0.93	0.00	0.00	0.93	0.00	0.00	0.00	0.93	0.00
1961		1.08	0.00	0.00	1.08	0.00	0.00	0.00	1.08	0.00

REMARKS: Layout is to scale as of 1951
