


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6801
TRUNK HIGHWAY 11
COUNTY Roseau
DISTRICT 2B

LIMITS: W. Co. Line - Jct. T.H. 32 in Greenbush.



YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o DIST.
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel Br. M-201	24' 16'	2"	No Record of Constr. 60 L. T.	1
1929	11-11-33-1	Grading	32'			2
1930	11-11-33-1	Gravel	24'	2"	1000 C.Y./Mile.	3
	(1)					
1931	11-11-33-1	Oil Tr. Gravel	24'	1"	13560 Gal./Mile. Maint. Dept.	4
1931		Oil Tr. Gravel	24'	1"	15211 Gal./Mile. Maint. Dept.	5
1936	11-11-46-2	Grading Br. 5552	32' 27'		50 B.S.	6
	(1)					
1936	11-11-46-2	Oil Tr. Gravel	24'	1"		7
					Maint. Dept.	
M	1941 A.F.E. 10	Bit. Seal Coat (High Type)	24'		RT-10, 3133 Gal./Mi. Agg. 107 C.Y./Mi. Maint. Dept.	8
M	1944 A.F.E. 4	Bit. Fog Seal (Spots)	22'		RT-420 Gal./Mi. Grav. 10 C.Y./Mi. Maint. Div.	9
M	1945 A.F.E. 4	Bit. Seal Coat	24'		RT-2161 Gal./Mi. Grav. 47 C.Y./Mi. Maint. Div.	10
M	1948 A.F.E. 4	Bit. Surf. Repair	24'		SC-3, 9531 Gal. Agg. 400 C.Y.	11
M	1970 A.F.E. 4	Bit. Fog Seal	24'		RCS-1, 14687 Gal. Agg. 342 C.Y.	12
M	1953 A.F.E. 817	Light Bit. Seal	24'		RT-3, 15761 Gal. Agg. 700 Tons	13
M	1956 A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 57144 Gal. Agg. 4642 Tons	14

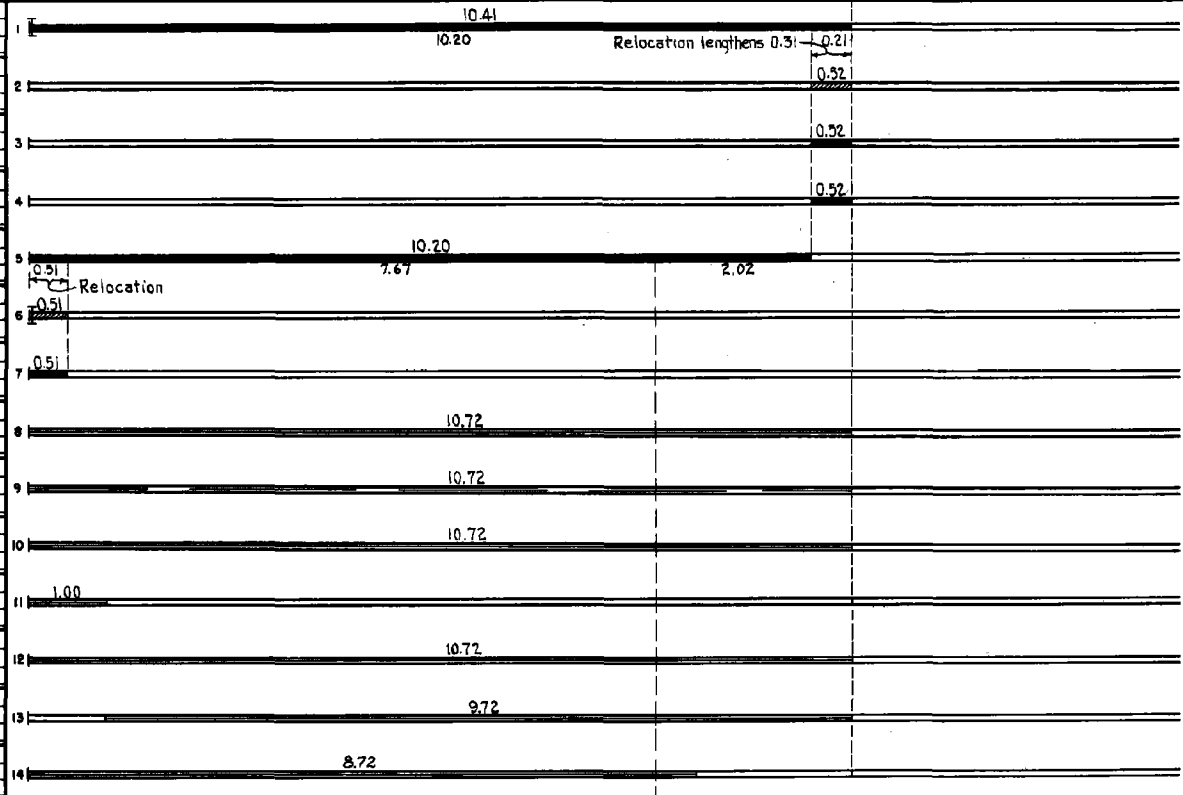

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1928	10.41	9.59	0.01	0.81	0.00	10.40	0.01	0.00	0.00
1929	1936	10.72	9.59	0.01	1.12	0.00	10.71	0.01	0.00	0.00
1937	1970	10.76	9.76	0.01	0.99	0.00	10.75	0.01	0.00	0.00
1971		10.82	9.82	0.01	0.99	0.00	10.81	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1936.
(1) This work not done under these project numbers but lies within the limits of these projects.

