


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8004
TRUNK HIGHWAY 71
COUNTY Wadena
DISTRICT 3A

LIMITS: Jct. T.H. 10 in Wadena - Jct. T.H. 227 in Sebeka.



YEAR BUILT	PROJECT N#	DESCRIPTION			CODE N#
		TYPE	WIDTH	THICKNESS	
1925	71=4-29-2	Grading Br. 4186 & 4187	32'	23"	131 L.T. & B.S. & 60 B.S.
1925	71=4-29-2	Clay	32'	2"	
1926	71=4-29-2	Gravel	24'	3 1/2"	1600 C.Y./Mile.
	(1)				
1930	71=4-29-2	Oil Tr. Gravel	50'	1"	13218 Gal./Mile. Maint. Dept.
	(1)				
1931	71=4-29-2	Oil Tr. Gravel	28'	1"	Maint. Dept.
C	8004-01	Grading Stab. Subgrade	32'	4"	
C	8004-01	Grading Gravel Surface	32'	1 1/2"	
C	8004-11	Grading (2) 8" Stab. Agg. Base (3) Bit. Surf. Treat.	V.V. 32'	2'-6" 3/4"	8" Stab. Grav. Shoulder 3 Rt. & Lt.
C	A.F.E. 7	Seeding			Seed supplied by R.S.D. (S.P. 8004-08) Maint. Dept.
M	1942 A.F.E. 5	Bit. Seal Coat	24'		AE-1, 359 Gal./Mi. Sand 103 C.Y./Mi. Maint. Dept.
M	1943 8004-14	Base Repair Bit. Surfacing (Spots)	26'	1"	
M	1946 A.F.E. 4	Spot Treat. Bit. Surf. Repair Spot Seal Coat	24'		RC3, 9375 Gal. Agg. 336 C.Y.
C	1947 8004-17	Base Repair (Spots) Bit. Resurfacing (Plant Mix)	24 1/2'	1 1/2" Added	
M	1949 A.F.E. 5	Bit. Seal Coat	24'		RC-082 28947 Gal. Agg. 1090 C.Y.

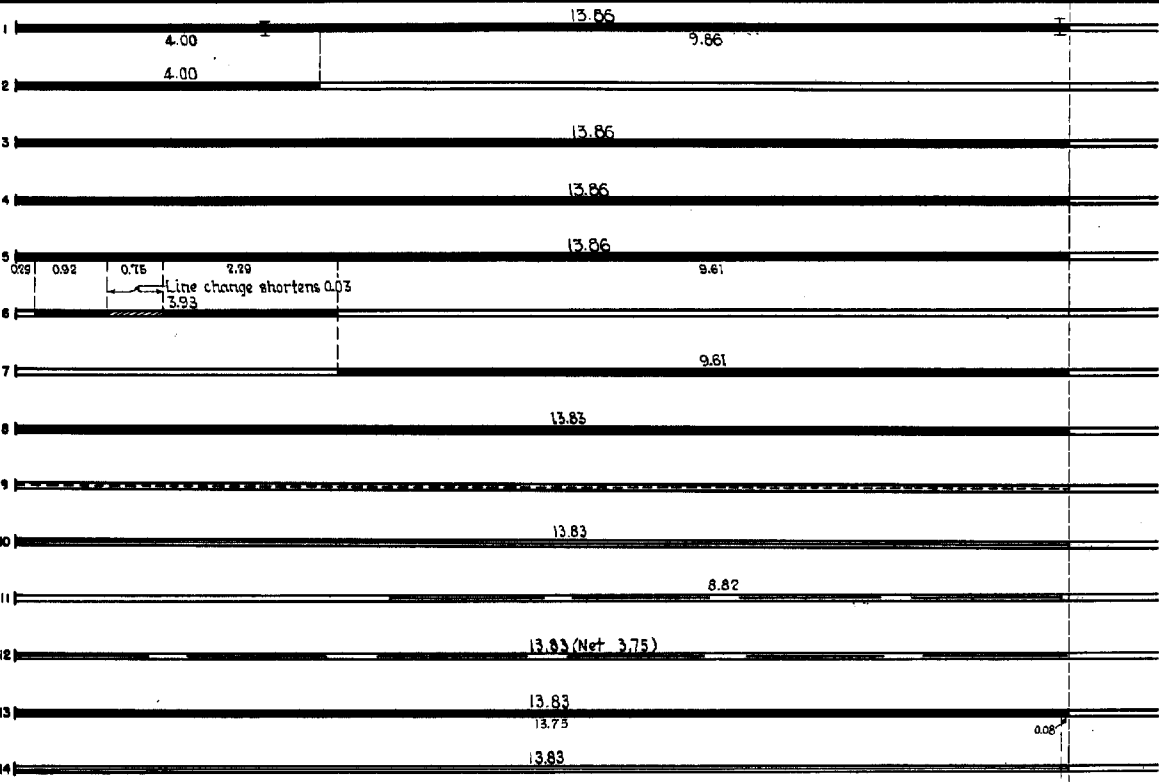

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1925	1939	13.86	11.51	0.05	2.45	0.01	12.56	0.04	1.45	0.00
1940	1962	3.83	1.44	0.03	2.35	0.01	12.43	0.04	1.36	0.00
1963		13.83	11.43	0.03	2.36	0.01	12.42	0.04	1.37	0.00

REMARKS: Layout is to scale as of 1925

(1) This work not done under this project number but lies within the limits of this project. (2) Grading of 0.29 Mi. only in Wadena. (3) 2" Stab. Base placed on portion for which the subgrade had previously been stabilized to a depth of 4" and 6" Stab. Base placed on balance.


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 0004
TRUNK HIGHWAY 71
COUNTY Wadena
DISTRICT 3A

LIMITS: Jct. T.H. 10 in Wadena - Jct. T.H. 227 in Sebeka

Ref. Pt. 225+00.068 - 238+00.894



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
M 1953	A.F.E. 605	Light Bit. Seal	24'		RCS-2, 23358 Gal. Agg. 1278 Tons
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC-2, 3500 Gal. Agg. 259 Tons
C 1956	8004-15	Drainage Ditch			
C&M 1959	8004-19 (1) 8004-21 A.F.E. 605	Grading & Bit. Surf. Br. 9797 Bit. Seal Coat	44' 30' 24'	1 1/2" 3/4"	2856 Gal. 66 Conc. S.S. RS-2, 29,655 Gal.
C 1963	8004-22 8004-80001	Plant Mix Bit. (Base) Plant Mix Bit. Br. 80001	28' 28'	1 1/2" 3/4"	155 Precast C.S.
C 1964	8004-24	Plant mix Bit.	44'	3"	
C 1978	8004-27	Bit. Shoulders	10'	1 1/2"	
C 1978	8004-28	Bit. Shoulders Right Turn Lanes	10' 12'	1 1/2" 1 1/2"	
M 1984	SF	Bit. Overlay	46'	2"	Sp. 2341 138 Ton
M 1986	SF	Bit. Overlay	var	1 1/2"	Spec. 2341
C 1992	8004-31	Mill & Bit. Overlay	24'	3"	Spec. 2341
C 1993	8005-13	Mill & Bit. Overlay	40'	2"	Spec. 2341
M 1995	8004-95068	Major Crack Repair			
M 1999	8004-99212	Grading Gravel Surfacing	6' 5'	1 1/2"	Class 1

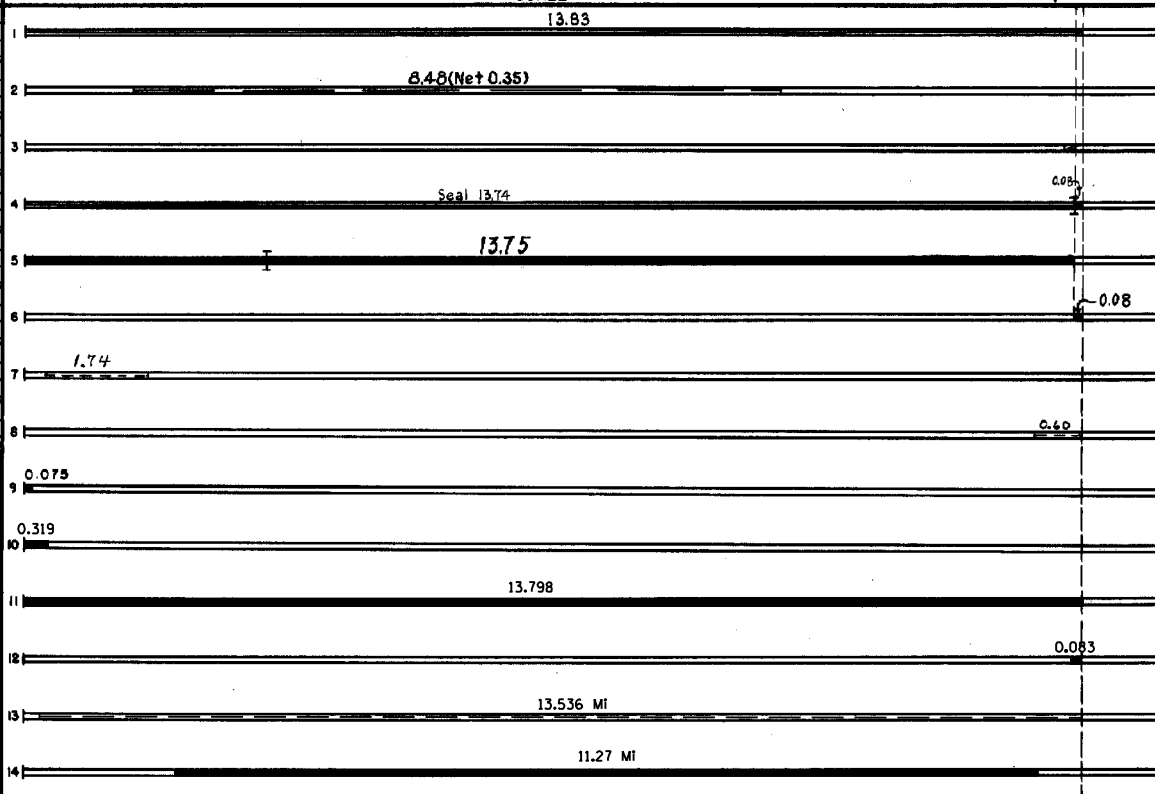

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1
(1) Contract not final but work substantially complete.

