


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8219
TRUNK HIGHWAY 244
COUNTY Washington
DISTRICT Metro

LIMITS: W. Co. Line (E. Jct. T.H. 120) - Jct. T.H. 96 in Dellwood
Ref. Pt. 002+00.537 - 007+00.279



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
		P.C. Concrete	20'		No Record of Const. Added in 1949	
1949	8219-01	Plant Mix Bit.	20'	1 1/4"	On Old P.C. Concrete	
1957	8219-03	Grading Gravel Base Mixed Bit. (Base)	42' 42' 26'	7" 1 1/2"	on 10' Sand-Gr. Subbase	
1957	A.F.E. 634	Guard Rail (2760')				
1959	A.F.E. 605	Light Bit. Seal	27'		RC-2, 3080 Gal. Agg. 112 C.Y.	
1963	8219-04	Plant Mix Bit Shoulders	24'	3 1/4"		
1973	8219-06	Bit. Overlay Gravel & Bit. Shldrs.	20' 5'	1"		
1983	8211-23	Intersection Rev. Bit. Surfacing Bit. Shoulders	24'	8 1/2" 1 1/2"	At Jct. T.H. 96	
1985	8219-16	Mill & Bit. Overlay Turn Lane Const.	24'	1 1/2"	Spec. 2341	
1986	8219-11	Grading Bit. Surfacing	52'	3 1/2" 3/4"	Spec. 2331 Spec. 2361	
1992	SF	Mill & Bit. Overlay		1"		
2001	8219-19	Milling Bit. Overlay	52'	2"	Spec. 2350	
2003	8219-20	Milling Bit. Overlay	24'	2"	Spec. 2360	
2010	8219-21	Micro Surfacing Seal Coat				

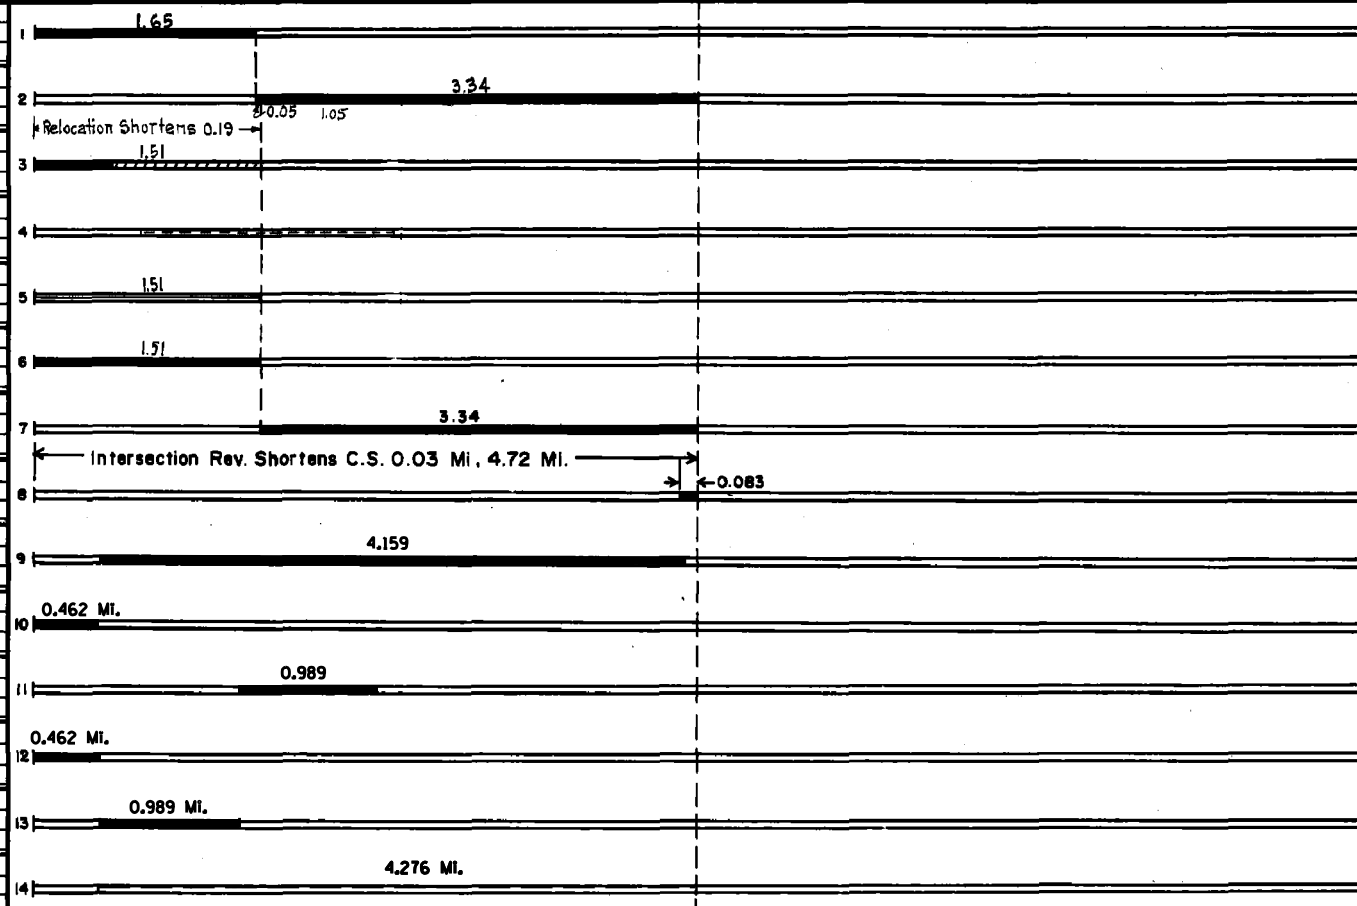

FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: Layout is to scale as of 1949
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1949	1950	4.99	1.58	0.00	3.41	0.00	4.99	0.00	0.00	0.00	
1951	1952	4.99	1.58	0.00	3.41	0.00	3.11	0.00	1.88	0.00	
1957	1959	4.80	1.28	0.00	3.52	0.00	2.81	0.00	1.99	0.00	
1960	1963	4.80	1.01	0.00	3.79	0.00	2.81	0.00	1.99	0.00	
1964		4.80	0.88	0.00	3.92	0.00	2.68	0.00	2.12	0.00	
