FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0904
TRUNK HIGHWAY 33
COUNTY Carlton
DISTRICT 1A

LIMITS: Jct. T.H. 61 - E. Jct. T.H. 210 at Iverson



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					No Record of Constr.	
		Gravel	24'	3"		
					Added in 1934.	
C		Gravel	24'	3"		
1940	A.F.E. 57	Bit. Surf. Treat.	21'	½"		
					Maint. Dept.	
M					SC-3, 4879 Gal./Mi.	
1941	A.F.E. 7	Bit. Retreat.	21'		Agg. 202 C.Y./Mi.	
					Maint. Dept.	
M					SC-3b, 2201 Gal./Mi.	
1942	A.F.E. 4	Bit. Retreat.	21'		Agg. 120 C.Y./Mi.	
					Maint. Dept.	
M		Spot Treat.			MC-2, 263 Gal./Mi.	
1944	A.F.E. 4	Bit. Surf. Repair	24'			
					Maint. Div.	
M		Spot Treat.			MC-2, 3672 Gal./Mi.	
1945	A.F.E. 4	Bit. Surf. Repair			Agg. 204 C.Y./Mi.	
					Maint. Div.	
M					SC-3, 19275 Gal	
1947	A.F.E. 4	Bit. Surf. Repair	22'		Agg. 1240 C.Y.	

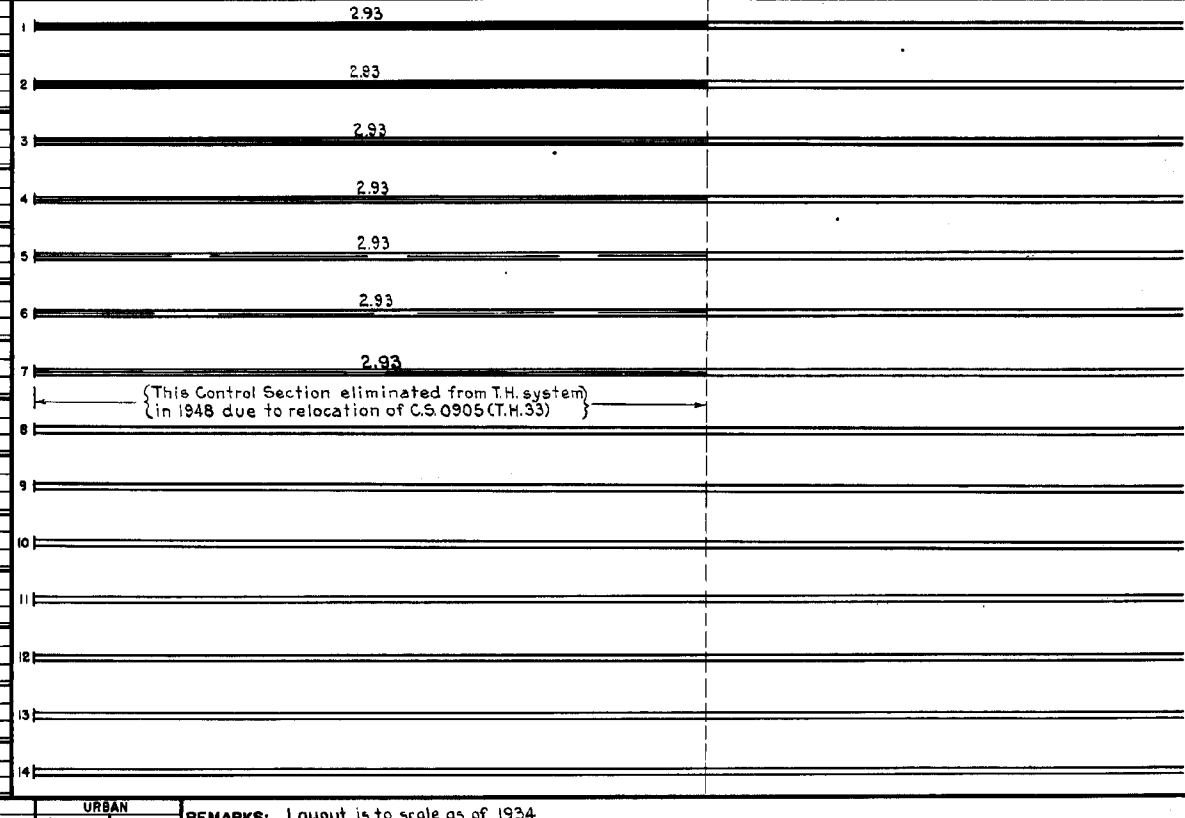

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1947	2.93	2.93	0.00	0.00	0.00	2.93	0.00	0.00	0.00
1948		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934
