FORM R.L.-7 REV. 3-58

SHEET 1 OF 1

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

# STATE OF MINNESOTA
## DEPARTMENT OF HIGHWAYS
## ROAD LIFE STUDIES
## CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3615
TRUNK HIGHWAY 53
COUNTY Koochiching
DISTRICT 1B

LIMITS: In International Falls
N. Jct. T.H. 11 — S. end International Bridge

Ref. Pt. 164+00.040 - 164+00.361

| YEAR BUILT | PROJECT NO | DESCRIPTION TYPE | WIDTH | THICKNESS | REMARKS |
|---|---|---|---|---|---|
| | | | | | No Record of Const. |
| 1958 | | Plant Mix Bit. | 41'-55' | 1½"-2½" | Added to system |
| | | Old Conc. Base (0.07 Mi.) | | | in 1959. |
| | | | | | No Record of Const. |
| | | Mixed Bit. | 40' | | Added to system |
| | | | | | in 1959. |
| C | | | | | |
| 1971 | 3615-02 | Plant Mix Bit. | 40'-55' | 5/8" | |
| M | | | | | |
| 1979 | 3615-03 | Resurfacing; AC | 44'-60' | 3/4" | AC Sp. 2361 174 Ton |
| | | | | | Tack Coat |
| S | | | | | |
| 2008 | 3615-05 | Milling | 41' | 3" | |
| | | Bit. Surfacing | 41' | 3" | Spec. 2360 |




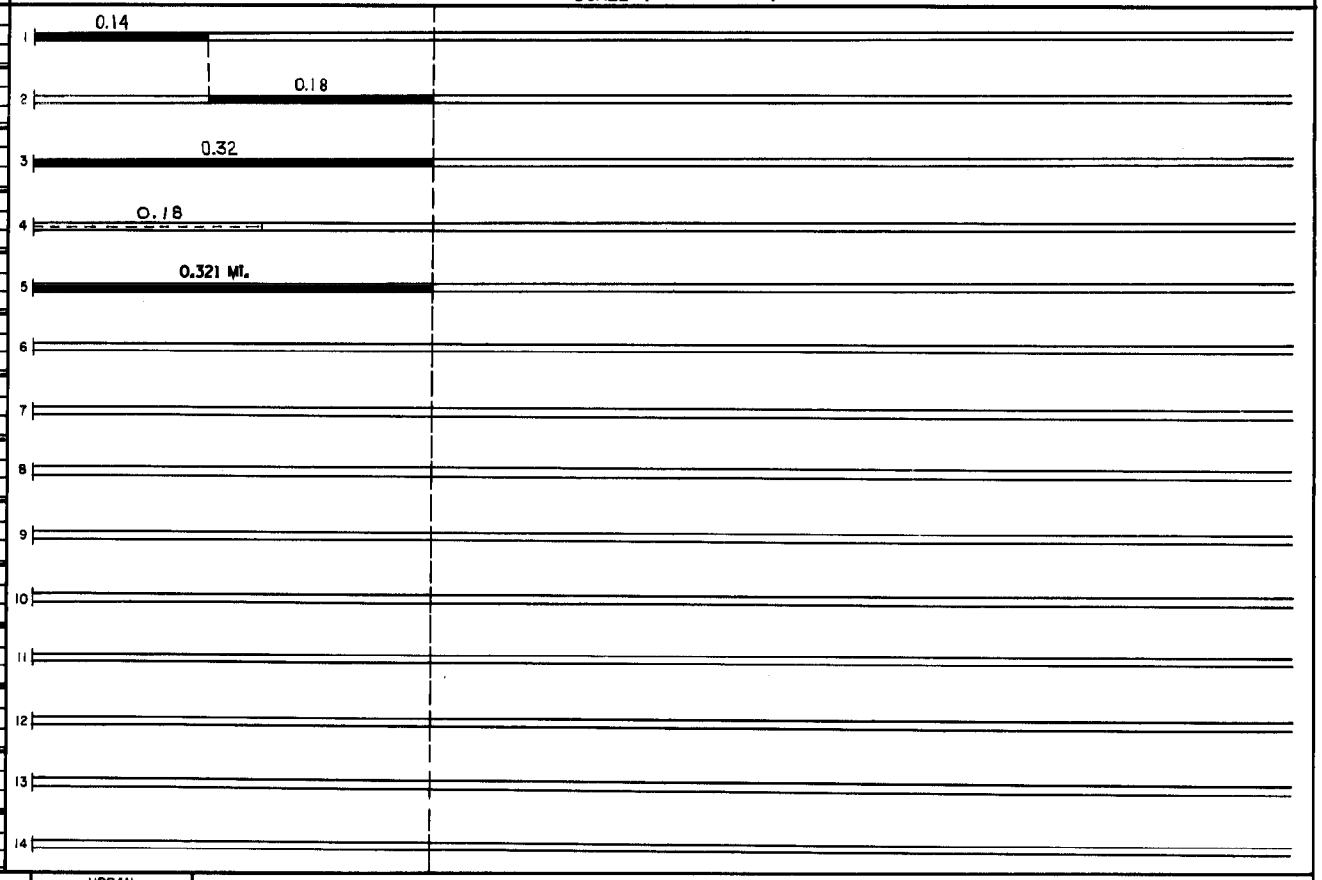


| YEARS FROM | YEARS TO | TOTAL MILES | UNINCORPORATED RDWY. MI. | UNINCORPORATED BR. MI. | INCORPORATED RDWY. MI. | INCORPORATED BR. MI. | RURAL RDWY. MI. | RURAL BR. MI. | URBAN RDWY. MI. | URBAN BR. MI. |
|---|---|---|---|---|---|---|---|---|---|---|
| 1959 | | 0.32 | 0.00 | 0.00 | 0.32 | 0.00 | 0.00 | 0.00 | 0.32 | 0.00 |

REMARKS: Layout is to scale as of 1959.
